


| ID | Description | Original Duration | Start | Finish |
|------------------------------|---|-------------------|-----------|-----------|
| Bid Pack 1- Site | | | | |
| 10 | Move out of Existing Fire Station | 20 | 03/21/22A | 04/15/22A |
| 20 | Site Package Permitting | 15 | 04/04/22A | 04/22/22A |
| 30 | SWPPP Permitting | 10 | 04/04/22A | 04/15/22A |
| 80 | Site Package Bidding | 10 | 04/04/22A | 04/15/22A |
| 70 | Mobilize to Site (Fences, Job Trailer, etc) | 3 | 04/18/22A | 04/20/22A |
| 90 | Demo Bid Day | 0 | 05/10/22A | |
| 100 | Establish GMP/ Buyout | 7 | 06/24/22A | 07/04/22A |
| 15 | Demo Existing Fire Station | 10 | 07/12/22A | 07/25/22A |
| 27 | RAP Bidding | 25 | 08/02/22A | 09/05/22A |
| 25 | Rammed Aggregate Piers Design | 5 | 10/07/22A | 10/21/22A |
| 26 | RAP Design Submittal Review | 10 | 10/26/22A | 11/08/22A |
| 28 | **Lead time for Electrical Gear** Awaitin | 275 | 10/31/22A | 12/13/23 |
| 50 | Mass Excavation | 5 | 11/03/22A | 11/09/22A |
| 60 | RAP Install | 10 | 11/14/22A | 11/25/22A |
| Building Construction | | | | |
| 77 | Construction Documents | 72 | 05/19/22A | 08/29/22A |
| 99 | CPT Testing | 4 | 07/08/22A | 07/13/22A |
| 103 | CPT incorporation by Geotech- Release | 13 | 07/14/22A | 08/01/22A |
| 120 | Bldg Bidding | 17 | 08/29/22A | 09/20/22A |
| 130 | Buyout/ Establish GMP | 5 | 09/21/22A | 10/20/22A |
| 110 | Bldg Permitting | 20 | 11/17/22A | 02/02/23A |
| 65 | Footings and Foundations | 35 | 11/28/22A | 03/20/23 |
| 67 | Underground Utilities | 25 | 03/21/23 | 04/24/23 |
| 68 | Slab on Grade | 15 | 04/25/23 | 05/15/23 |
| 69 | Structural Steel Install | 20 | 05/16/23 | 06/12/23 |
| 75 | Exterior Metal Stud Framing (Structural) | 15 | 05/23/23 | 06/12/23 |
| 76 | Roof Framing & Decking | 15 | 06/13/23 | 07/03/23 |
| 82 | Exterior Sheathing | 10 | 06/13/23 | 06/26/23 |
| 87 | Interior Metal Stud Framing | 30 | 06/13/23 | 07/24/23 |
| 83 | Curtain Wall/ Storefront Systems | 40 | 06/27/23 | 08/21/23 |
| 85 | Veneer Brick Masonry | 15 | 06/27/23 | 07/17/23 |
| 93 | Storefront Window Systems | 20 | 06/27/23 | 07/24/23 |
| 94 | Exterior Soffit ACM/ Other Finishes | 10 | 06/27/23 | 07/10/23 |
| 79 | Layout MEP Openings | 2 | 07/04/23 | 07/05/23 |
| 81 | Rough Plumbing | 60 | 07/04/23 | 09/25/23 |




Start Date: 03/02/22
 Finish Date: 02/13/24
 Data Date: 02/07/23
 Run Date: 02/07/23

North Davis Fire District
 Construction Schedule
 Feb. 7, 2023

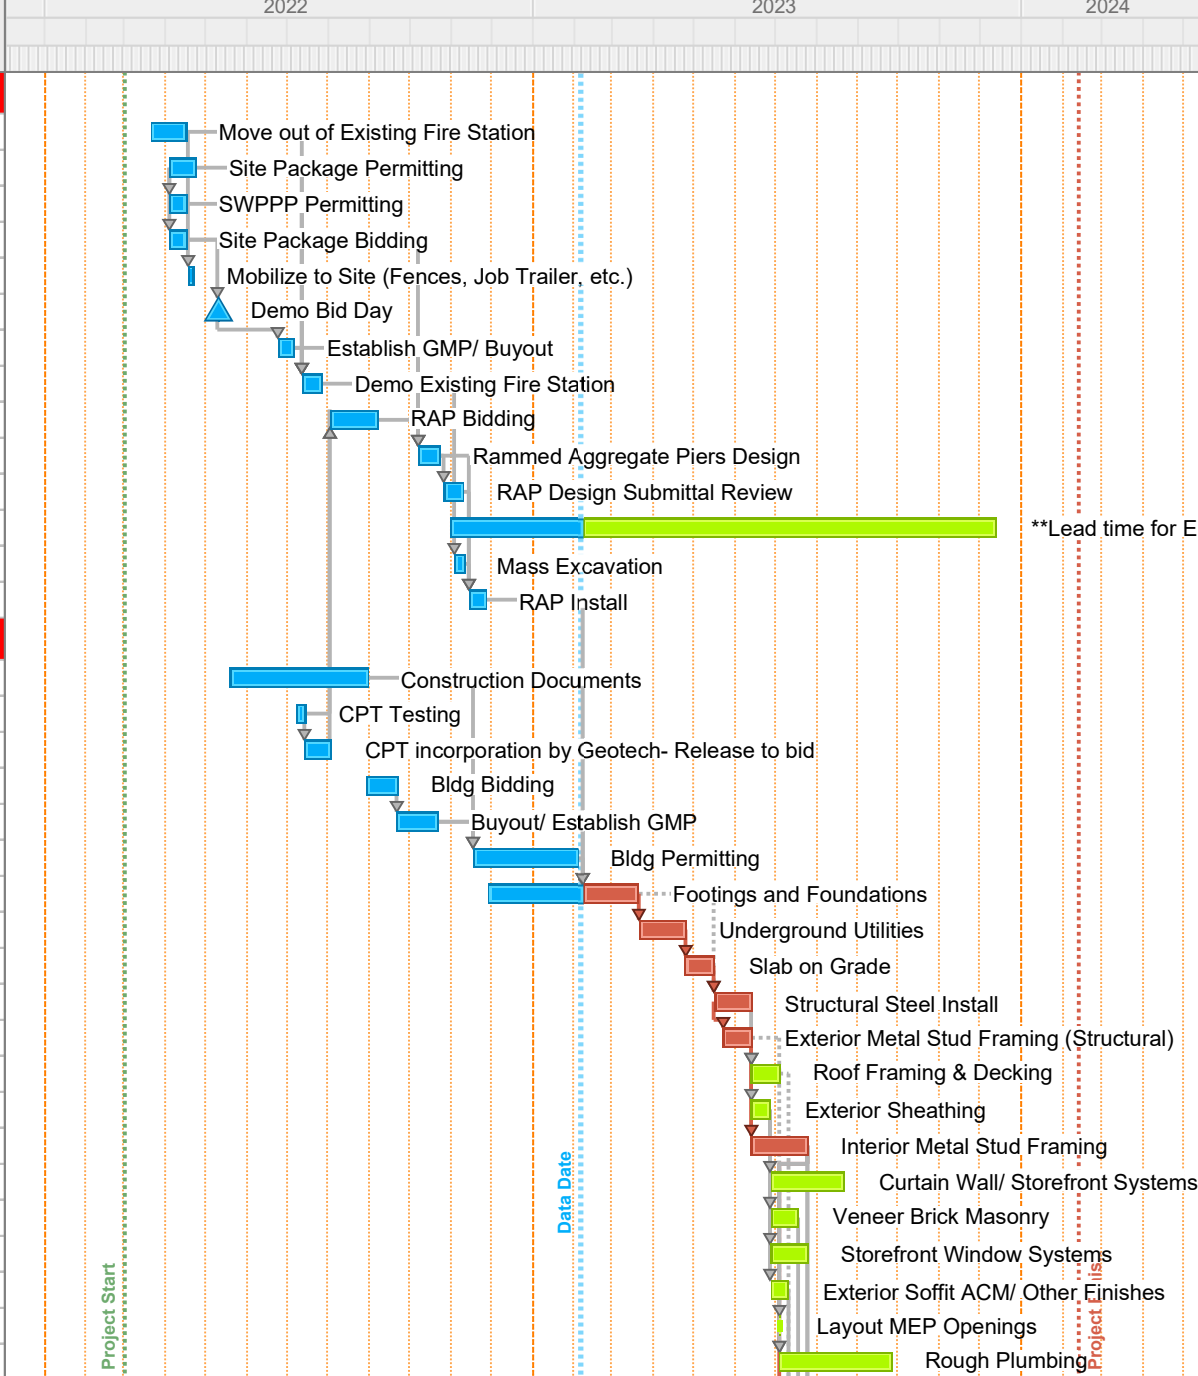

| ID | Description | Original Duration | Start | Finish |
|-----|---------------------------------------|-------------------|----------|----------|
| 84 | Rough Electrical | 60 | 07/04/23 | 09/25/23 |
| 78 | Roofing | 10 | 07/11/23 | 07/24/23 |
| 88 | ACM Exterior Wall Panels | 10 | 07/18/23 | 07/31/23 |
| 86 | Rough Mechanical | 20 | 07/25/23 | 08/21/23 |
| 95 | Install HM Door Frames | 5 | 07/25/23 | 07/31/23 |
| 89 | 4 Way Inspections | 3 | 09/26/23 | 09/28/23 |
| 91 | Hang & Tape Drywall | 35 | 09/29/23 | 11/16/23 |
| 92 | Insulation | 10 | 09/29/23 | 10/12/23 |
| 96 | Painting | 15 | 11/17/23 | 12/07/23 |
| 97 | Ceramic Tile | 15 | 12/08/23 | 12/28/23 |
| 102 | Finish MEPF | 15 | 12/08/23 | 12/28/23 |
| 105 | Acoustic Ceilings- T Grid | 10 | 12/08/23 | 12/21/23 |
| 108 | Startup HVAC Systems with constructio | 3 | 12/08/23 | 12/12/23 |
| 98 | Millwork | 5 | 12/29/23 | 01/04/24 |
| 101 | Flooring | 10 | 01/05/24 | 01/18/24 |
| 106 | Countertops | 5 | 01/12/24 | 01/18/24 |
| 104 | Interior Doors and Hardware | 10 | 01/19/24 | 02/01/24 |
| 107 | Final Cleaning | 5 | 02/02/24 | 02/08/24 |
| 111 | Startup and Test and Balance | 5 | 02/02/24 | 02/08/24 |
| 109 | Occupancy Inspections | 3 | 02/09/24 | 02/13/24 |
| 112 | Turn Over to Owner | 0 | | 02/13/24 |

| Site Construction | | | | |
|-------------------|-----------------------------------|----|----------|----------|
| 116 | Demo Existing Sidewalks | 5 | 04/17/23 | 04/21/23 |
| 119 | Complete Remaining Site Utilities | 10 | 04/17/23 | 04/28/23 |
| 118 | Prep & Place Curb and Gutter | 4 | 05/01/23 | 05/04/23 |
| 125 | Place Site Concrete and Sidewalks | 25 | 05/05/23 | 06/08/23 |
| 126 | Install Pavers | 4 | 06/09/23 | 06/14/23 |
| 127 | Road Base and Asphalt | 5 | 06/09/23 | 06/15/23 |
| 129 | Irrigation | 10 | 07/03/23 | 07/14/23 |
| 128 | Landscaping | 15 | 07/17/23 | 08/04/23 |

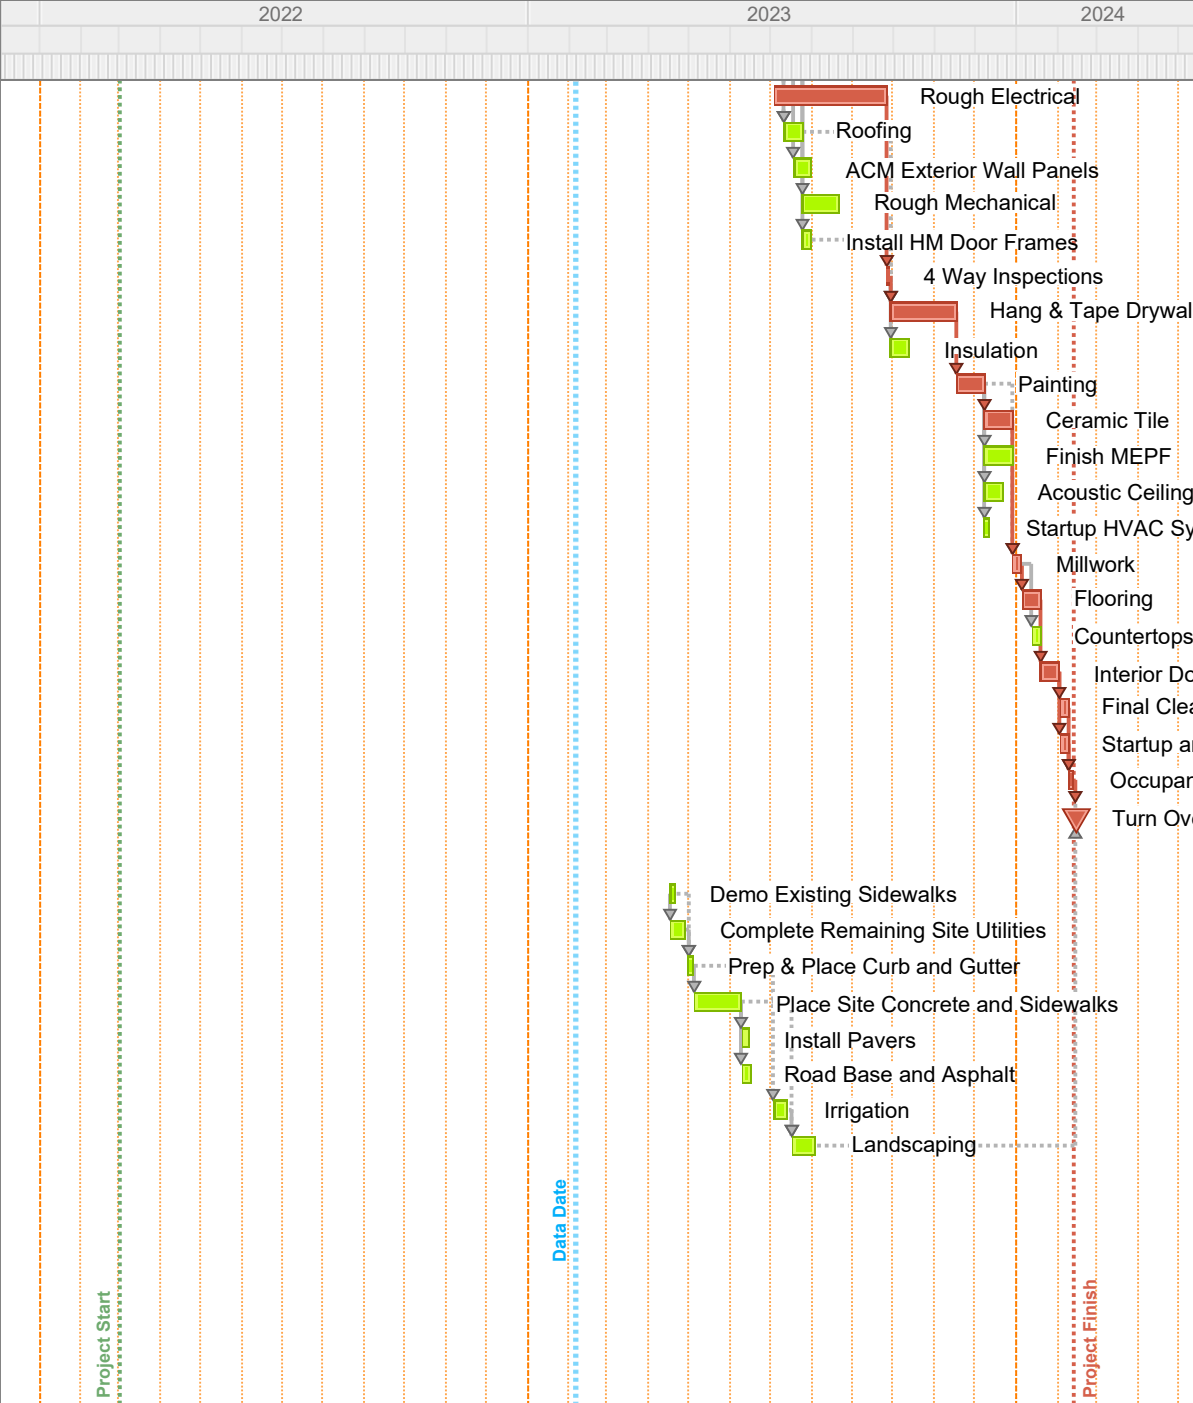

Start Date: 03/02/22
 Finish Date: 02/13/24
 Data Date: 02/07/23
 Run Date: 02/07/23

North Davis Fire District
 Construction Schedule
 Feb. 7, 2023

